


Proposed Subcontractors

Trade	Subcontractor	Location / Address
Civil Works	McLennan Earthmoving	South Grafton NSW 2460
Concreting	Farlow Concreting	Coffs Harbour NSW 2450
Electrician	Advanced Electrical & Data	Junction Hill NSW 2460
Hydraulics	Drew Walker Plumbing	Valla NSW 2448
Roofing	Mid Richmond Plumbing	Coraki NSW 2471
Windows	G James	Lismore NSW 2480
Linings	Jensen Plastering	Swan bay NSW 2471
painting	Premier 3D Painting	Goonellabah NSW 2480
Epoxy Floors	East Coast Epoxy Floors	Port Macquarie NSW 2444
Structural Steel	Sable	Macksville NSW 2447
Metalwork	Commercial Metalwork Services	Nambucca Heads NSW 2448
Fencing	Warren McCann Fencing	Grafton NSW 2460
Landscaping	Great Gardens Landscaping	Sapphire Beach NSW 2450
Joinery	Viison Kitchens	Taree NSW 2430
Irrigation	Yamba Pumps & Irrigation	Yamba NSW 2464
Pest Control	Termimesh	Port Macquarie NSW 2444

Grafton Greyhound Racetrack & Kennel Building

Head Construction Programme


ID	Task Name	Start	Finish	Duration
1	PROJECT ESTABLISHMENT	Mon 30/11/20	Fri 30/04/21	100 days
2	Letter of Award	Mon 30/11/20	Mon 30/11/20	1 day
3	Development of management plans	Tue 1/12/20	Mon 7/12/20	5 days
4	Procurement of trades & supplies	Tue 1/12/20	Mon 4/01/21	20 days
5	Pre-commencement notifications	Tue 1/12/20	Tue 1/12/20	1 day
6	Site possession	Tue 1/12/20	Mon 7/12/20	5 days
7	SITE ESTABLISHMENT & EARLY WORKS	Tue 8/12/20	Fri 11/12/20	4 days
8	Site amenities	Tue 8/12/20	Wed 9/12/20	2 days
9	Environmental & other controls	Thu 10/12/20	Thu 10/12/20	1 day
10	Demolition	Fri 11/12/20	Fri 11/12/20	1 day
11	SUPER STRUCTURE	Fri 11/12/20	Wed 3/03/21	54 days
12	Strip site	Fri 11/12/20	Fri 11/12/20	1 day
13	Bulk earthworks - Building	Mon 14/12/20	Fri 18/12/20	5 days
14	Survey setout	Mon 21/12/20	Tue 22/12/20	2 days
15	Inground services	Wed 23/12/20	Tue 5/01/21	5 days
16	Footing excavation	Wed 6/01/21	Fri 8/01/21	3 days
17	FRP Building slab	Mon 11/01/21	Tue 26/01/21	12 days
18	Masonry	Wed 27/01/21	Tue 16/02/21	15 days
19	Building Framing	Wed 17/02/21	Tue 23/02/21	5 days
20	Roof install	Wed 24/02/21	Mon 1/03/21	4 days
21	Window & Door install	Wed 17/02/21	Mon 22/02/21	4 days
22	External Cladding	Tue 2/03/21	Wed 3/03/21	2 days

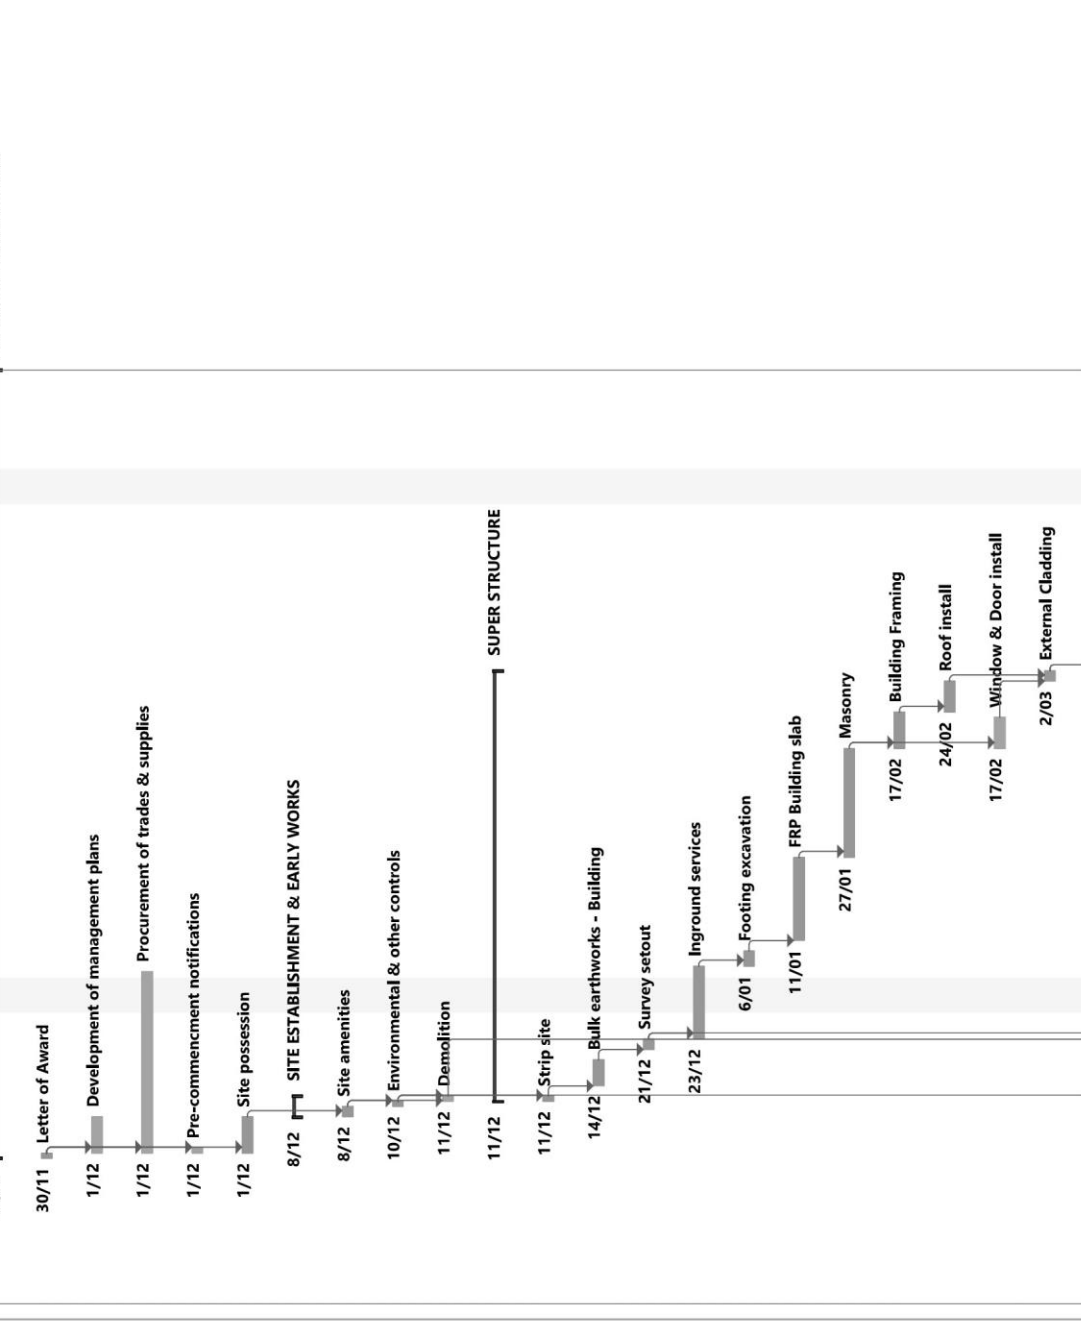

Task	Project Summary	Manual Task	Start-only	Deadline	Manual Progress
Task	Project Summary	Manual Task	Start-only	Deadline	Manual Progress
Split	Inactive Task	Duration-only	Finish-only	Critical	Critical
Milestone	Inactive Milestone	Manual Summary/Rollup	External Tasks	Critical Split	Critical Split
Summary	Inactive Summary	Manual Summary	External Milestone	Progress	Progress

Grafton Greyhound Racetrack & Kennel Building

Head Construction Programme

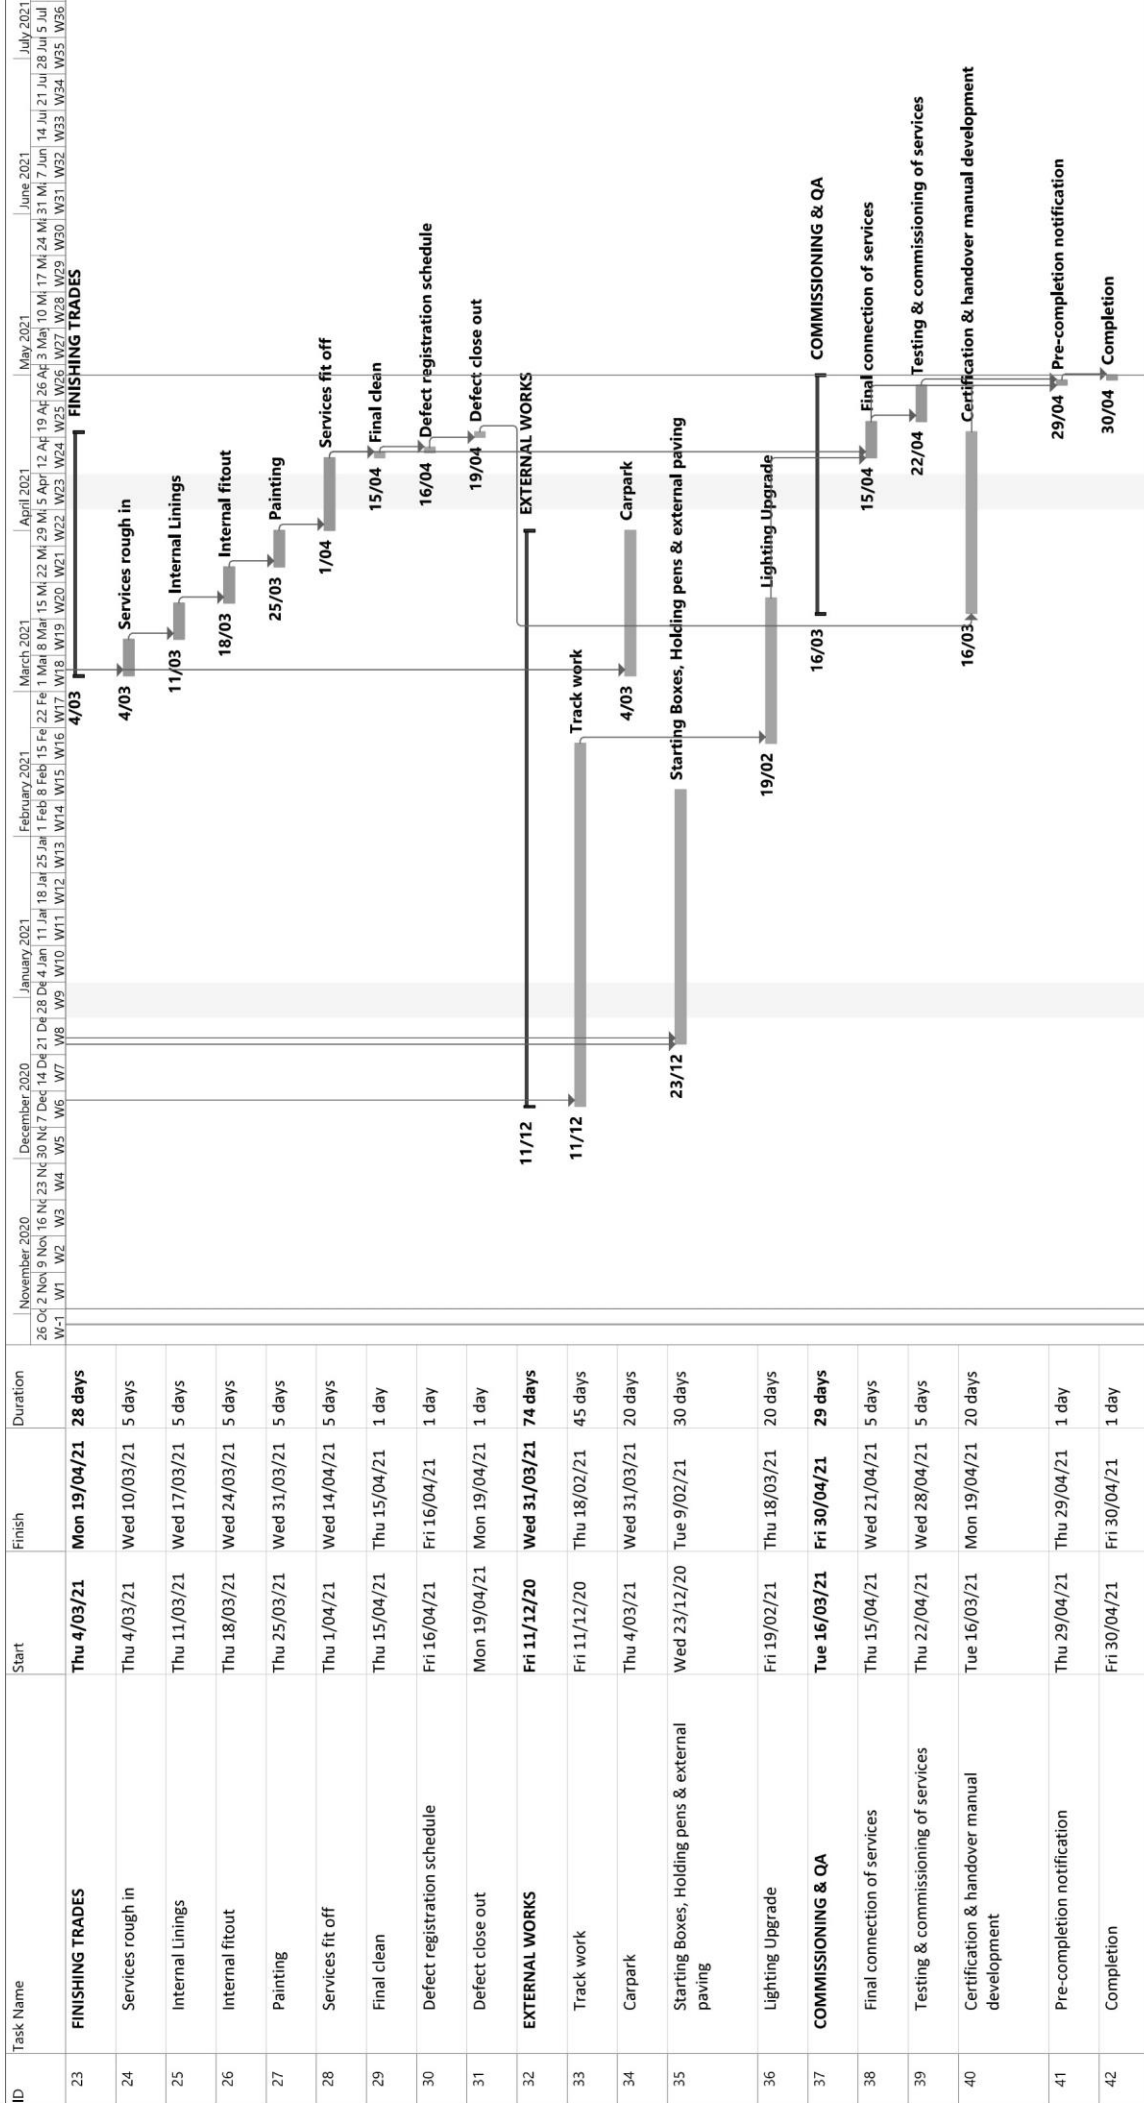

Legend for Gantt chart symbols:

- Task: Solid grey bar
- Split: Dotted line
- Milestone: Diamond
- Summary: Thick solid bar
- Project Summary: Thin solid bar
- Inactive Task: Dotted line
- Inactive Milestone: Diamond
- Inactive Summary: Thin solid bar
- Manual Task: Solid grey bar
- Duration-only: Thin solid bar
- Manual Summary/Rollup: Thick solid bar
- Manual Summary: Thin solid bar
- Start-only: Thin solid bar
- Finish-only: Thin solid bar
- External Tasks: Thin solid bar
- External Milestone: Diamond
- Deadline: Vertical line
- Critical: Thick solid bar
- Critical Split: Dotted line
- Progress: Thin solid bar
- Manual Progress: Thin solid bar
